

XOSERVE

DSC Delivery Sub-Group

July 2026





1. General Meeting Administration

1b

[Previous DSG Meeting Minutes](#)

[Action Updates](#)



The DSG Actions Log will be published on the DSG pages of [Xoserve.com](https://xoserve.com)



SECTION 2: Change Development

02

2a. New Change Proposals

2b. Undergoing Solution
Options Impact Assessment
Review



SECTION 2: Change Development

2a. New Change Proposals

- 2a.i XRN 6106 DDP Release 3 2026-27

2b. Undergoing Solution Options Impact Assessment Review

- None for this meeting



XRN 6106 DDP Release 3 2026/2027

Customer Parties	Impacted parties
Shipper	X
Distribution Network Operators (DNOs)	X
National Gas Transmission	
IGTs	X
This vote is to approve the change into development	

Change Type	Regulatory
Priority	High
Proposer	CDSP
Change Proposal	Link to CP

Change Description	
The request for this Change Proposal is to ensure that there is visibility to ChMC of the changes within scope of DDP Release 3 2026/27 – this aims to provide transparency so the rationale of the priority being applied to DDP scope can be clearly understood. Following prioritisation discussions at ChMC and with Xoserve, in release/sprint 3 (Aug-Sep), we intend to deliver XRN 6001 and features prioritised by Customers. The detail is in the Proposed Release section below.	Core: • XRN 6001: Modification 0909 - Refining the Class 2 Individual Valid Meter Reading Requirement Performance Measures Class 2/3 reclassification updates Stretch (Priority 1) Shippers • Addition of 'Previous MAM code' Meter Registration Details report Networks • New report 'Active Sites With No Meter Report' IGTs • CSEP search functionality for upstream references and Nested CSEPs Stretch (Priority 2) Shippers • New report highlight AQs of 1
DSC Service Area Associated Funding Split	Funded via annual DSC DDP change delivery costs, which forms part of the General Change Investment within BP26
Proposed Funding split from Proposer	N/A



SECTION 3: Detailed Design

03

3a. Design Considerations

3b. Requirements Clarification



SECTION 3: Detailed Design

3a. Design Considerations

- 3a.i XRN 5949 - New Priority Consumer Category related to Community Heating - Part A

3b. Requirements Clarification

None for this meeting



XRN5949 – New Priority Consumer Category
related to Community Heating

Detailed Design Overview



Change Background

Priority Consumers are certain gas Supply Meter Points (SMPs) for Industrial and Commercial sites that have been identified to be deemed priority during a national gas emergency to ensure that they are mitigated from any direction to cease off taking gas.

Currently there are three categories of Priority Consumers, as defined under the Secretary of State's [letter of direction](#) to Gas Transporters, dated October 2022:

Category A: Relevant customers where a failure in the supply to their premises could put lives at risk.

Category B: Relevant customers for which the sudden loss of gas causes or threatens to cause serious damage, for an unacceptably prolonged period, to human welfare, the environment or the security of the United Kingdom that cannot be reasonably mitigated.

Category C: Relevant customers taking over 2 million Therms (58.6m kWhs) per annum for which the sudden loss of gas would result in repair or replacement costs amounting to 10% or more of the Site Fixed Tangible Asset Value.

Following on from the Gas Task Group led by National Gas Transmission & Distribution Networks, and in conjunction with the Department for Energy Security & Net Zero (DESNZ), it has been recommended that a new Priority Consumer category (Category D) related to Community Heating is introduced within Central Systems to support downstream industry processes, e.g. Load Shedding activities in the event of a Gas Deficit Emergency.

To facilitate this, DSC Change Proposal XRN5949 was raised and developed with a Solution Option Change Pack being issued in [April-26](#) and Solution Option 1 approved to move into Detail Design phase at Change Management Committee (ChMC) in May-26.



Change Background

In line with discussions at ChMC surrounding potential delivery options and the immediate industry requirement for the introduction of Category D (CAT D) into the Priority Consumer process by Winter 2026, it is proposed that XRN5949 be delivered in 2 parts.

Part A Tactical: Interim manual process for handling the introduction of Category D requests (including Bulk Upload), amending the Proforma for requesting Priority Consumer Sites and ensuring category D SMPs are visible to industry participants via existing manual reporting.

Part B Enduring: Amending the Supply Point Register to accept Category D as an allowable value (including file format amendments for industry consumption) and ensure these values are automatically visible within UK Link Portal and feed GES Priority Consumer indicator.

Detail Design Change Pack issued for consultation on 13th July outlines the changes being proposed as part of Part A Tactical, another DDCP will be produced for Part B Enduring to be issued in line with industry timelines for an agreed implementation date within 2027.

Note: File format changes to introduce a new Category D as an allowable value will be incorporated in the Detail Design of Part B Enduring and is out of scope for Part A Tactical.

Part A – Tactical Process Overview

This will be a temporary offline process, time-limited to only operate until the Part B Enduring process is implemented. This temporary tactical process will handle the day-to-day requests to add, update or remove a site's "Community Heating Priority Consumer Category D" ("CAT D") indicator. For the avoidance of doubt, Category A, B & C will not be impacted and requests related to these will be processed as normal.

There are three main elements to Part A Tactical, these are as follows:

- **Bulk Data Load** – Due to the numbers of expected requests for inclusion of SMPs into Category D, it is proposed that we carry out a bulk upload of known SMPs needing this category assigned.
- **Operational Processing** – Amendments to the day-to-day Priority Consumer process facilitated by the CDSP.
- **Industry Reporting** – Amendments made to reporting functionality to ensure the manual gathering of Category D SMPs are included within external reporting for stakeholders to have visibility of these sites.

Part A – Tactical Process-Bulk Data Load

The CDSP will provide the capability to request a bulk list of sites to be added and associated with CAT D. The facility is sized to cater for a bulk add of a total of up to 12,000 individual sites, submitted by a multiple number of requestors. The facility is not designed to handle updates to/from CAT D to/from another category, or the removal of CAT D; such requests must be made via the individual requests made via the “Priority Consumer Application Form”.

- The tactical bulk data receipt facility will only require a list of valid MPRNs to be securely submitted to the CDSP.
- CDSP performs manual validation of the request (as described in Detailed Design Change Pack) and rejections will be notified back to the requestor.
- The bulk data receipt facility will be available for a limited period of two (2) weeks post implementation to support load of data into the process. All requests submitted after this two (2) week period must be raised using the Priority Consumer Application Form.
- The list of MPRNs submitted by a requestor is expected to be pre-approved by DNs, needing no accompanying Supporting Information, and which will not require any further validation/approval of the request, nor for the CDSP to refer the request to a DN for validation/approval.
- It is assumed that the MPRN data to feed the Bulk Data Load will be provided by the Shippers. We are to be engaging with Shippers in the coming weeks (Shipper Constituency and AdHoc session if needed) to discuss this requirement and agree suitable timelines for receipt / transfer of data for processing.

Part A – Tactical Process-Operational Processing

The process is sized to cater for up to 20 Category D individual site requests manually per month submitted via “Priority Consumer Application Form”, the following stakeholders can use this form to submit Cat D requests to the CDSP during this interim period.

- **Shipper:**
 - Sends to CDSP, by manual “Priority Consumer Application Form”* submitted by email, a request to add a CAT D indicator to a site
 - Optionally: Shipper can provide Supporting Information (SI) to support the request
- **Gas Transporter (GT):**
 - Sends to CDSP, by manual “Priority Consumer Application Form”* submitted by email, or by email without a Pro Forma, a request to add CAT D indicator to a site
 - Optionally: GT can provide Supporting Information (SI) to support the request

*“**Priority Consumer Application Form**” will be revised and uploaded to Xserve.com prior to implementation to allow CAT D requests to be submitted



Part A – Tactical Process-Operational Processing

- CDSP performs manual validation of the received request (as described in Detailed Design Change Pack).


Note: Where a site already has a priority consumer category (e.g. A, B or C) assigned, as per the current rules, the latest requested category, if approved, will be assigned to the SMP and the existing category value end dated.

- CDSP manually refers requests submitted by Shippers to the GT associated with the site via email which will include the Supporting information (SI) where provided by Shippers.
- The outcome of the referral will be relayed to requesting Shipper and CDSP will record the CAT D indicator to site (in a temporary datastore) for all successful referrals.
- For all requests submitted by GTs for a site on their own GT network, CDSP will record the CAT D indicator in a temporary datastore.
- CDSP will accept a request from a requestor to update/remove a CAT D indicator of a site or amend the existing CAT A/B/C to the new CAT D.

X Part A – Tactical Process-Industrial Reporting

- CDSP currently provides a suite of Priority Consumer Reports to different stakeholders and CDSP will be producing a replica set of these existing reports that will contain all MPRNS that are confirmed or pending referral confirmations for Category D.
- For the avoidance of doubt, these new Cat D reports will be issued out to stakeholders alongside the existing reports for the interim period, meaning customers will receive two sets of reports. One set reporting only CAT D sites, another set reporting CAT A/B/C sites.
- The naming convention for the new set of reports will include 'CatD' in the report name.
- e.g. Priority_Consumers_Report_CatD_SHP_YYYY-MM-DD-HH-MM-SS
- Please note where the same MPRN is classified as Category D in temporary data store and classified as CAT A/B/C within UKLink, this could result as a duplicate in existing and new reporting suites.

X Part A - Tactical – Process Overview

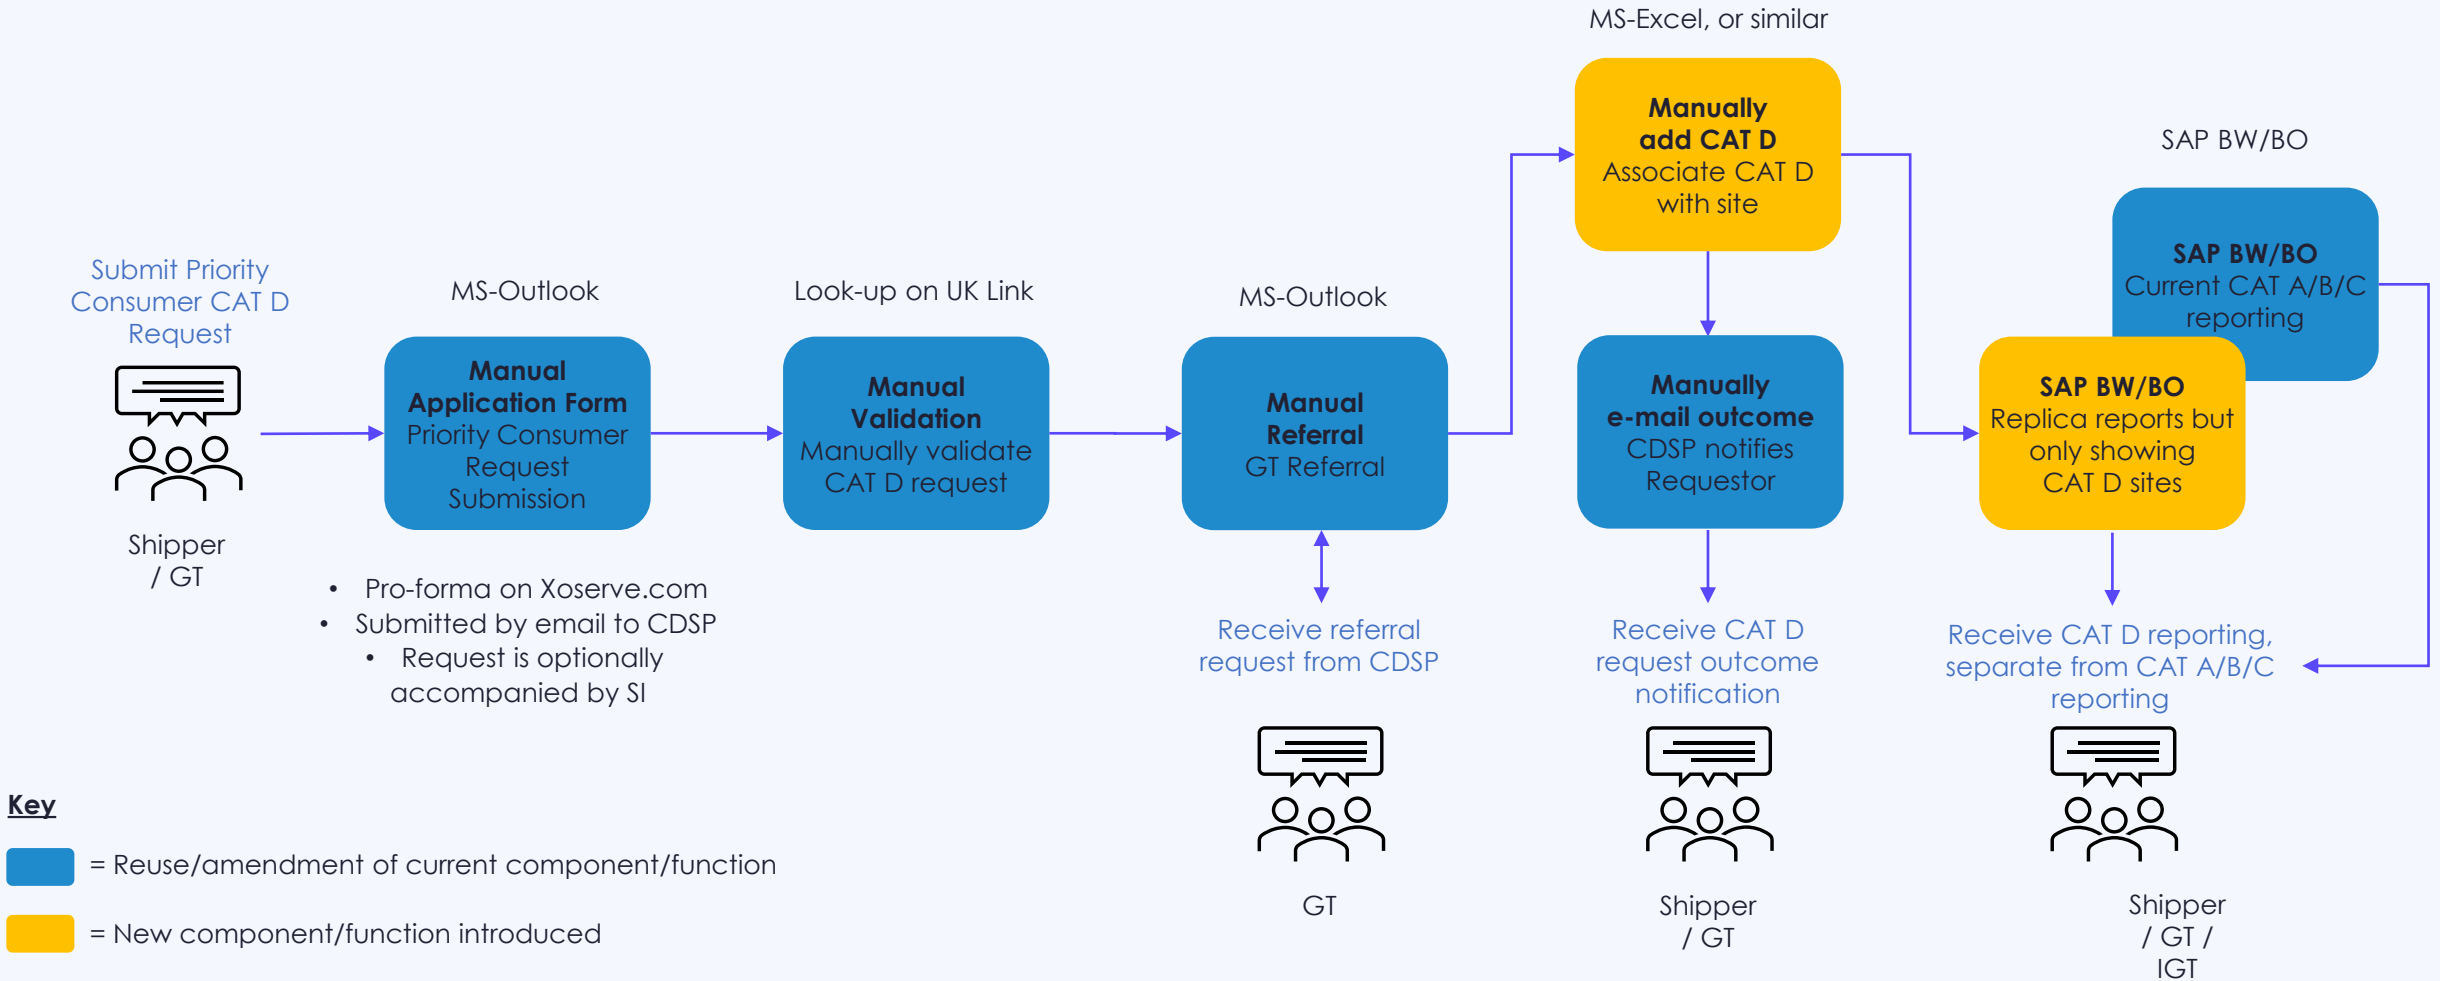



Part A – Tactical Process-Additional Information

- The recording of Priority Consumer CAT D data will be undertaken outside of UK Link and will be recorded within CDSP in a temporary datastore securely.
- While the Tactical TO BE Process is operating, outbound files containing a Priority Consumer Category (e.g. TMC, TRF) will not show CAT D sites until Part B Enduring goes live. Shippers will not know that they are acquiring a CAT D site at Change of Shipper/Supplier from TMC, TRF files until the monthly Shipper report is received.
- The presence of CAT D Priority Consumer Category against a site will not be indicated in GES (includes the online portal and Supply point enquiry API), or UK Link files, until Part B Enduring goes live.

Part A – Tactical Process - Assumptions

- Categorisation of an MPRN as Category D is the responsibility of the submitting Shipper or Gas Distribution Network (GDN). It is assumed that all submitted MPRNs have been correctly identified as Category D and CDSP will not determine, validate or distinguish between the different heat network types.
- Supporting Information (SI) to accompany a CAT D request is optional for requests submitted via Priority Consumer Application Form and is not applicable for the requests submitted via bulk process.
- The CDSP does not hold information, within the CDSP estate, to approve a CAT D request. Requests will be referred to a GT for approval for individual requests only.
- Ongoing validation/re-validation of meter point data will not be undertaken, e.g. to remove the CAT D indicator if the meter point status is no longer recorded as “live.”

X Next Steps

- The Detailed Design Change Pack (DDCP) was issued for consultation on **13th July 2026**
- Shippers, DNOs and IGTs will vote on the outcome of the DDCP consultation at ChMC on **12th August 2026**





Section 4: Release/Project Updates

04

4a. XRN 5983 – February 26 Major release

4b. XRN 6045 – June 26 Major Release

4c. XRN 6065 – Minor Release 16

4d. February 2027 Major Release (Scope for Information)



RAG Status	Overall Project RAG status											
	Schedule				Risks and Issues				Costs			
	Status Justification											
Schedule	The scope of February 26 Major Release was presented for approval at the ChMC meeting on 10/09/25. Overall release is tracking to target. Project was successfully implemented 27/02/26, Post Implementation Support completed 10/05/26 and is now currently in closedown due to complete 28/08/26. Progress Update: • XRN5906, 5872, 5914/5922 has completed Post implementation support (PIS) and been handed over into BAU 29/05/26. • Project is on track to closedown 28/08/26.				Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug ✓ Design Mon 28/07/25 - Thu 30/10/25 ✓ Build Fri 31/10/25 - Mon ✓ PIS Fri 27/02/26 - Fri 29/05/26 Closedown Mon 01/06/26 - Fri 28/08/26 ✓ Start Up and Initiation Mon 01/09/25 - Mon 01/12/25 ✓ Test Mon 15/12/25 - Fri ✓ Implementation Fri 27/02/26 ● Complete ● On Track ● At Risk ● Overdue Implementation date 27th February, contingency date 6th March							
Risks and Issues	N/a											
Costs	Changes are currently delivering with projected costs.											
Scope	XRN5906 - Extending the PC4 Read Submission Window. XRN5872 - Updates to the AQ Amendments Process. XRN5914/XRN5922 - Shorten of the current LIS (Line in sand) date to 2-3 years & amend the LIS to rolling Period.											



XRN 6045 – June 26 Major Release- Status Update

RAG Status	Overall Project RAG status		
	Schedule	Risks and Issues	Costs
	Status Justification		
Schedule	The scope of June 26 Major Release was presented for approval at the ChMC meeting on 11/02/2026. Overall release is tracking to target; project is planned implement on 26/06/2026. Progress Update: June is tracking at Green and Implementation is on track for 26th June 2026. Both XRN5805 & XRN5702 have completed all testing and are deployed to ready for Go live Decision in June ChMC: None	● Complete ● On Track ● At Risk ● Overdue Implementation date 26th June 2026, contingency date 3rd July 2026	
	Risks and Issues	N/A	
Costs	Forecast to complete delivery against approved BER		
Scope	XRN5702 – Update to assess the replacement of Facsimile as a form of communication (Modification 0864S) XRN5805 - Alternative Solution to address instances where VBA macros are present in DN Templates		



XRN6065 – Minor Release 16 - Status Update

RAG Status	Overall Project RAG status		
	Schedule	Risks and Issues	Costs
	Status Justification		
Schedule	The scope of Minor Release 16 was presented for approval at the ChMC meeting on 08/04/26. Overall release is tracking at Amber; Build completed on 05/06/26. Test in progress tracking at Amber due to defects impacting testing. Recovery plan in progress. Progress Update: XRN 6081A Build completed, testing is in progress. Decision in July ChMC: None	Start 23/02/26 Mar '26 ✓ START UP / INITIATION 02/03/26 - 17/04/26 ✓ DESIGN 02/03/26 - 30/03/26 Apr '26 ✓ BUILD 30/03/26 - 05/06/26 Jun '26 TEST 08/06/26 - 07/08/26 Today Jul '26 Aug '26 IM 10 15/08/26 - 11/09/26 Sep '26 CLOSEDOWN 14/09/26 - 23/10/26 Oct '26 Finish 23/10/26 Overall Timeline Implementation Go Live 14/08/26 ● Complete ● On Track ● At Risk ● Overdue Implementation date 14th August	
Risks and Issues			
Costs	UK Link costs covered under Service and Operate funding		
Scope	XRN 6081A – Meter Reading Service Improvement A - Fix Historic NDM Check to Check Reconciliation Periods - Tactical Solution		

February 2027 Major Release Updated Scope

Release	February 2027 Major Release
Implementation Date	26 th February 2027

XRN / Ref	Title	Proposer	Benefitting	Funded by	Estimated Cost	Design Approval	BER Approval
5949	New Priority Consumer Category related to Community Heating	National Gas	All	Service Area 3	£120-£230k (HLSO)	12/08/26	TBC
5950	DSC Invoice Number generation review	Xoserve	Shipper, DN, NG	Service Area 10	TBC – HLSO publication expected 13/07	TBC	TBC
5955	Private networks duplicate MPRNs - options for long-term fix	Cadent	DN	New Service Line Anticipated	TBC – HLSO publication expected 13/07	TBC	TBC
5987	Modification 0915 – Debt Relief Scheme Payment (DRSP)	Northern Gas	Shipper, DN, IGT	New Service Line Anticipated	TBC	TBC	TBC

Decision	Presented for information
----------	---------------------------

February 2027 Major Release Scope Update

Scope Update

- There are currently four candidates for inclusion within the scope of this release, all of which are at verifying phases within the process:
 - XRN 5949 – Change is being delivered in 2 phases; initial tactical is targeted for October; with the enduring solution being targeted for February 27, DDCP for initial phase to be considered for approval at August ChMC.
 - XRN 5950 – Solution Options are due for publication on 13th July, with approval targeted for August ChMC; Detailed Design is likely to require some changes to UKL documentation, therefore, timescales for inclusion in February are tight.
 - XRN 5955 - Solution Options are due for publication on 13th July, with approval targeted for August ChMC.
 - XRN 5987 – Solution Options publication has yet to be finalized, potential impact to UKL documentation depending on the option chosen.




Section 5: Change Pipeline

05

Change Pipeline

X 2026/27 Forward View - Change Delivery Plan

April 26 – March 27

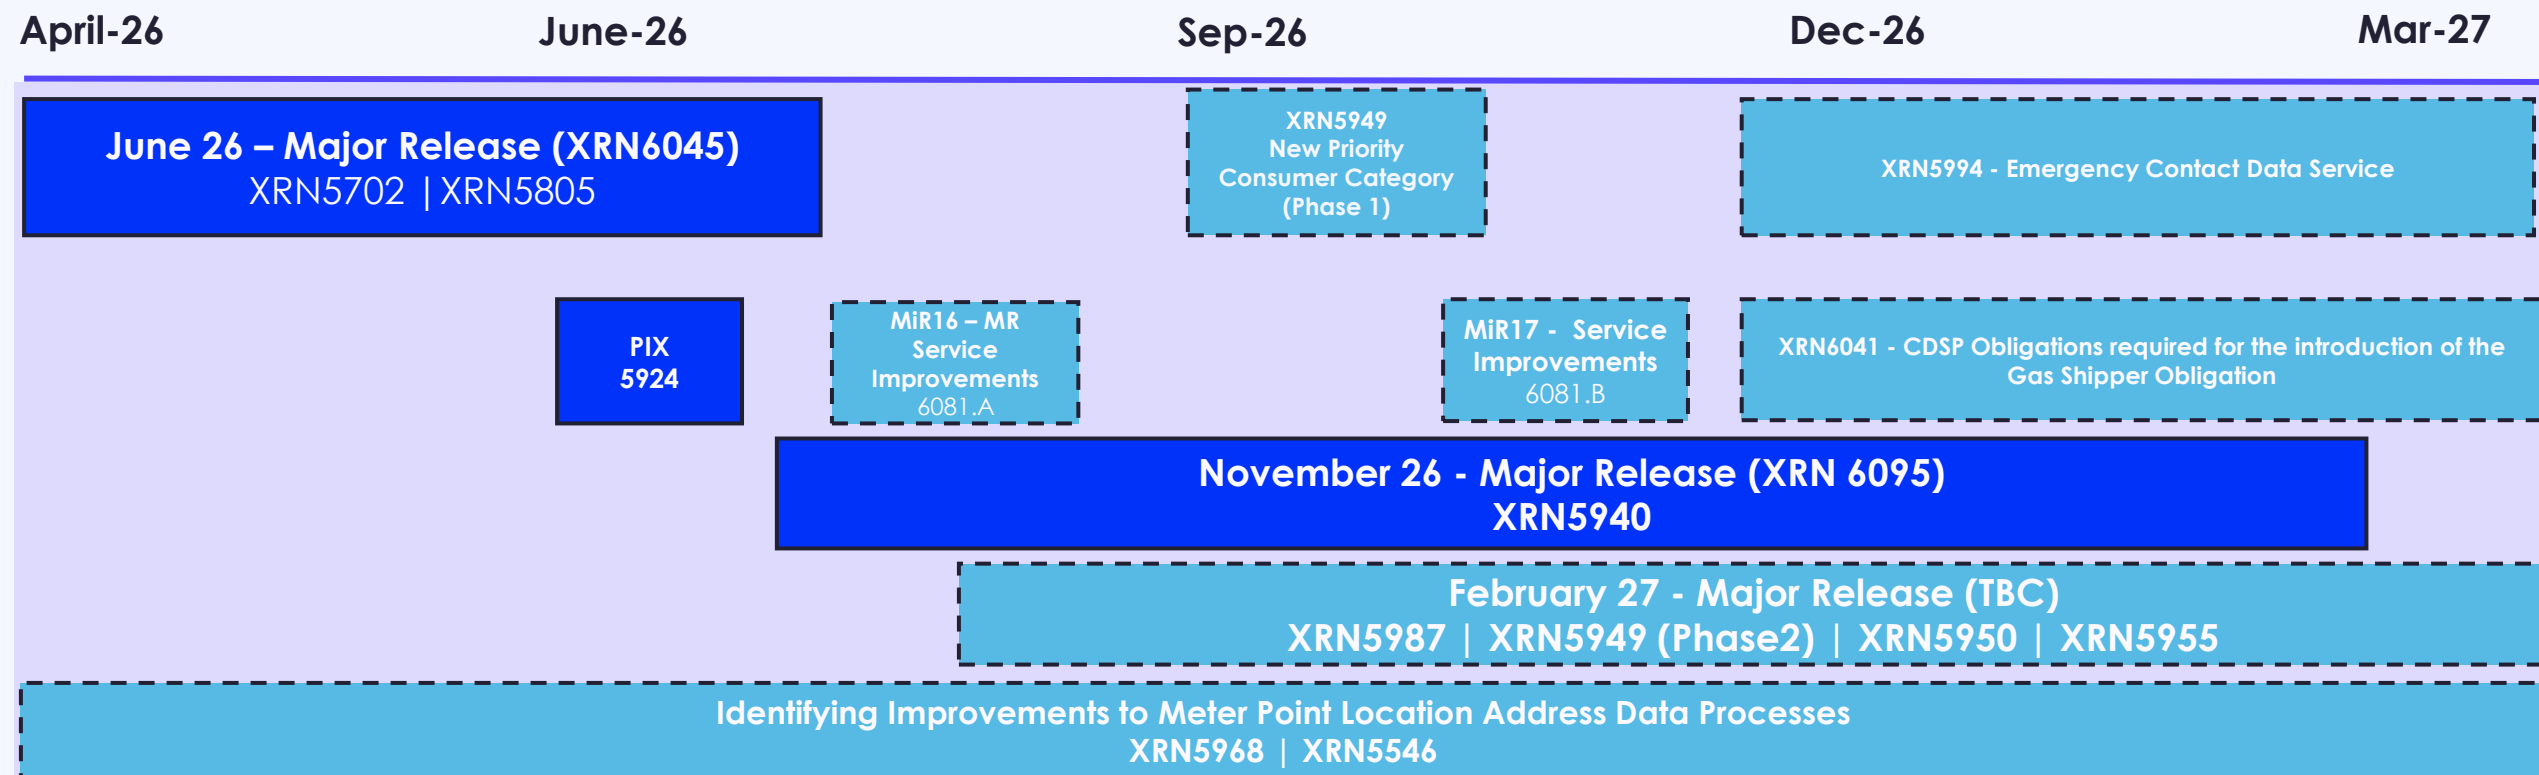

Delivery Key

- = Firm Implementation Date – Funding Approved by ChMC and / or Non-Negotiable Industry Implementation Date in place
- = Indicative / Target Implementation Date – Changes are planned for delivery – Funding not yet approved by ChMC
- = Implemented Change / Release

Change Delivery Plan – April 2026 – March 2027

XRN	Change Title	Proposer	Benefit / Impact	Funding	HLSO Max Cost	Target Delivery Date	Release Type	Firm / Indicative
5702	Mod0864S - Update to assess the replacement of Facsimile as a form of communication	NGT	All DSC Customers	Shipper DN	£158k	26 June 2026	Major	Firm
5805	Alternative Solution to address instances where VBA macros are present in DN Templates	WWU	DN	DN	£160k	26 June 2026	Major	Firm
5924	Physical Information Exchange (PIX) Ongoing Support Options	Xoserve	All	TBC	N/A	31 June 2026	Adhoc	Firm
5810	Theft of Gas (ToG) DN Calculation Tool	Cadent	DN	DN	N/A	31 July 2026	Adhoc	Indicative
6081 A	Meter Read Service Improvements Part A Fix Historic NDM Check to Check Reconciliation Periods - Tactical Solution	Xoserve	Shipper DN	N/A	N/A	August 2026	Minor	Indicative
6081 B	Meter Read Service Improvements Part B Reconciliation of Multiple Read Replacements – Historic Reporting and Tactical Solution	Xoserve	Shipper DN	N/A	N/A	September 2026	Minor	Indicative
5949	New Priority Consumer Category related to Community Heating (Phase 1)	NGT	All DSC Customers	TBC	£230k	September 2026	Adhoc	Indicative
5940	Mod0890 – Addition of Consumption Adjustment and Updated Meter Readings to initiate an AQ Calculation	Centrica	Shipper DN	TBC	£270k	18 December 2026	Major	Indicative
6041	UNC Modification 0922 (IGT UNC Modification 180) – CDSP Obligations required for the introduction of the GSO	CDSP	ALL DSC Parties	TBC	TBC	December 2026	Adhoc	Indicative
5994	Emergency Contact Validation Service	Cadent	Shipper DN	TBC	£170k	January 2027	Adhoc	Indicative
5987	Modification 0915 – Debt Relief Scheme Payment (DRSP)	NGN	Shipper DN IGT	NGT DN		February 2-27	Major	Indicative
5949	New Priority Consumer Category related to Community Heating (Phase 2)	NGT	All DSC Customers	TBC	£230k	February 2027	Major	Indicative
5950	DSC Invoice Number generation review	CDSP	Shipper DN NGT	TBC	TBC	February 2027	Major	Indicative
5955	Private networks duplicate MPRNs - options for long-term fix	Cadent	DN	DN	TBC	February 2027	Major	Indicative

Change Backlog – Prioritised Service Changes ‘In Progress’

XRN	Change Title	Proposer	Benefit / Impact	Funding	Status	July 26 - ChMC Update
<u>6000</u>	Modification 0908 – Removal of DNO meter reading obligations resulting from non-provision of a Valid Meter Reading by a Shipper	WWU	Shipper DN IGT	DN	Requirements	Change Proposal created to enable CDSP solution to be progressed in adherence to the related UNC Modification which has been approved. Transition arrangements being discussed ahead of agreeing implementation approach.
<u>5972</u>	CDSP provisions to support new Supplier Deed of Undertaking (DoU) Licence Condition (9a)	Cadent	DN IGT	DN	Requirements	Change Proposal raised on behalf of DNs to ensure new Deed of Undertaking arrangements are put in place with Supplier organisations. Analysis on Invoicing processes (charge types) to be performed and validated with DNs.
<u>6079</u>	UNC 0926S Maintenance criteria for Emergency Contact data held in Central Systems	Cadent	Shipper DN IGT	Shipper DN	Requirements	Change Proposal created to enable CDSP solution to be progressed in adherence to the related UNC Modification
<u>6067</u>	Facilitating Biomethane entry into the GDN by exporting methane from the GDN into the NTS via Compression (Modification 0894)	Cadent	Shipper DN NGT	TBC	Requirements	Change Proposal created to enable CDSP solution to be progressed in adherence to the related UNC Modification
<u>6066</u>	Facilitating Biomethane entry into the GDN by exporting methane from the GDN into the NTS via Compression (Modification 0894A)	National Gas Transmission	Shipper DN NGT	TBC	Requirements	Change Proposal created to enable CDSP solution to be progressed in adherence to the related UNC Modification
<u>5569</u>	Contact Data Provision for IGT Customers	BUUK	IGT	IGT	Solution Assessment	Solution Option issued for consultation in May '25 Change Pack – next steps to be confirmed following change pack decision and agreement on how to progress.
<u>5968</u>	Identifying improvements to Meter Point Location Address Data processes	Cadent	DN	DN	Analysis	Parent Change Proposal raised to perform analysis and make recommendations on changes that can be implemented to the Address Amendment process.
<u>6039</u>	Provision of IGT SMP Data to DNs	NGN	DN IGT	DN	Requirements	Change Proposal raised to progress solutions that enable DNs the ability to receive IGT SMP data. Requirements definition has commenced and solution assessment due to take place in June.
<u>6056</u>	Introduction of new Supply Meter Point status of 'IS' (Isolation) - Cleanse and remove obsolete 'CL' (Clamped) status	Cadent	DN IGT Shipper	DN	Requirements	New Change Proposal raised to progress solution that enables DNs and other industry stakeholders the ability to acknowledge a Supply Meter Point Status of Isolation. Target June 2027 Implementation, subject to relevant approvals.

Change Backlog – ‘On Hold’ Details

XRN	Change Title	Proposer	Benefit / Impact	Funding	HLSO Max Cost	July 26 ChMC Update
<u>5616</u>	CSEP Annual Quantity Capacity Management	WWU	DN IGT Shipper	DN IGT	*£260k revised following design	Agreed following August bi-party CSEP meeting that change will remain on hold whilst data cleansing activities were progressed.
<u>5546</u>	Resolution of Address Interactions between DCC and CDSP	Xoserve	DN IGT Shipper	Shipper	N/A	N/A – performing analysis on data extracts provided by DCC Incorporate findings into Address Management Project (XRN5968)
<u>5471</u>	DSC Core Customer Access to Data	CDSP	Shipper DN IGT	IGT Shipper DN	TBC	Low Priority – CDSP raised Change Proposal
<u>5806</u>	CDSP Solution to enable exit of application of User Premises Termination Notice (UPTN)	NGT	All DSC Customers	TBC	TBC	Change Proposal raised to analyse process and solution impacts that may be necessary to facilitate exit – analysis being planned in with relevant resource

Update provided via Action 0602: CDSP (KG) to consider reasons, solutions and/or a removal process to provide further clarity/justification for the aged on-hold Changes.



Section 6: AOB

06

6.a November 26 Project update – Delivery Timeline for XRN 5940 - Addition of Consumption Adjustment and Updated Meter Readings to initiate an AQ Calculation Month (Modification 0890)

6.b UK Link Sustain – Outages

6.c Xoserve Website - Change Register Enhancement

6.a November 26 Project
update – Delivery Timeline

Verbal update – Rob Westwood



UK Link Sustain

Extended Implementation Outage



X UK Link Sustain: Extended Outage

An upgrade to a number of our core applications (ISU, BW, AMT & PO) is taking place on Friday 28th and Saturday 29th August 2026.

This is a planned activity to ensure we sustain these critical components and continue to provide fully supported CDSP services.

The activity requires an extended outage which is anticipated to be completed by 09:00 on Saturday 29th August.

During this outage period, the in-scope UK Link applications being upgraded will not be available, with all inbound files received after 21:00 on Friday 28th August being held within IX and remaining unprocessed until the applications are restored at 09:00 on Saturday 29th August.

No outbound files will be sent during the outage period. Upon completion of the upgrade, a catch-up exercise will take place to process the held inbound files, resulting in a delay to receiving response files. We expect standard service to be resumed within the day on Saturday 29th August.

Note: Outage timings stated above are contingent on the upgrade completing successfully. In the event that a system rollback is required during cutover, the outage window will be extended, with service restoration expected by 13:00 on Saturday 29th August.



X UK Link Sustain: Held File Types

The following file types will not be processed during the outage window on Friday 28th August. All files received during this period will be held and processed once the system is restored at 09:00 on Saturday 29th August:

SPA

AES, AQR, BRN, BRO, BRR, CFR, CGI, CIN, CNR, CT3, DDU, DES, EDL, EWS, IDL, SSR, TER, TRF, WAO

RGMA

JOB, JRS, MAM, ONJ, UPD, UPR,

Metering

CRA, DLC, MRA/MDP, SFN, UBR, UDR, UMR, URN

Demand Estimation

AIA, AWV, CWF, CWV, FWV, WCF

FWACV

AI, Y0

Note: MDS, AAQ and SIF/SIR will be preponed and processed before the outage commences, alongside any other SLA critical files.

*Further impacted file types may be identified following completion of Implementation Dress Rehearsal 2 (IDR2) activities that are scheduled to take place throughout July 2026.



X UK Link Sustain: File Processing Order

Once the system is restored at 09:00 on Saturday 29th August, files will be processed in the following priority order:

Inbound File Types:

- AHD
- FHD
- BRN
- CSS Messages
- DLC
- AI
- Y0

Outbound File Types:

- AIA
- CWF
- IDL
- EDL
- EWA
- DDU

Note: Files will be processed in batches of 200 – 300, ensuring a maximum file size of 10MB. Standard service is expected to be fully resumed within the day. Remaining file types not listed above will be processed following completion of the priority jobs.



6.c Xoserve Website - Change
Register Enhancement

Verbal update – Karen Gray



Section 7: Annex

07

7a. [ChMC Update](#)

7b. [Rec Update](#)

7c. [POAP](#)
